



VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsess7012@gmail.com • Web : www.vsss.org
Fb : www.facebook.com/vsssindia • Blog : vsssindia.blogspot.in

Date: 31/03/2023

To
Shri Giriraj Kumar Mundhra
& The Trustees
Udyogi Foundation Trust
294, B.B Ganguly Street
2nd Floor, Kolkata.

Progress Report: School Building Construction for Khanpur Vivekananda Vidya Mandir under the direct management of Vivekananda Swasthya Seva Sangha.

Project Name: Construction of School Building for Khanpur Vivekananda Vidya Mandir under the direct management of Vivekananda Swasthya Seva Sangha.

Funded By: Corporate Social Responsibility (CSR) fund of Udyogi Foundation Trust, 294, B.B Ganguly Street, 2nd Floor, Kolkata.

Period: Financial Year 2022 - 2023

Introduction: The construction of the school building is part of a CSR activity by Udyogi Foundation Trust and joint initiative between Vivekananda Swasthya Seva Sangha and Udyogi Foundation Trust, aimed at improving educational infrastructure in the locality mainly in the areas of Khanpur, Block – Dhaniakhali, Dist – Hooghly, Pin – 712308, West Bengal, India. The project started in January 2022 and is being closely monitored for timely completion and adherence to quality standards.

Construction Progress:

1. Site Preparation: The project commenced with site clearance and levelling, followed by soil testing and surveying activities. This phase was completed on schedule to ensure a solid foundation for construction.
2. Structural Design and Approval: The architectural design and structural plans were prepared by experienced professionals, ensuring compliance with safety regulations, and maximizing the building's efficiency. The designs were approved by relevant authorities before the commencement of the construction phase.



VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsess7012@gmail.com • Web : www.vsss.org
Fb : www.facebook.com/vsssindia • Blog : vsssindia.blogspot.in

3. Building Construction: The construction work commenced in February 2022. The building is being constructed using high-quality materials and under the supervision of skilled workers and engineers. Progress has been smooth, and the construction is currently on track.

4. Foundation and Superstructure Work: The foundation work, including excavation and concrete pouring, has been completed successfully. The superstructure work for the Ground plus two floor building, involving the construction of columns, beams, plinth beam or slab, lintel, windows, doors, brick masonry work, walls, wall plastering, flooring, staircases, roofing, and water proofing. The construction team was focused on maintaining quality and adhering to safety protocols.

5. Plumbing and Electrical Installations: Simultaneously, plumbing and electrical installations are being carried out partially. The experts are ensuring that the installations meet the required standards for functionality, safety, and energy efficiency. Few works are still pending as on 31st March 2023.

6. Exterior and interior finishing: Simultaneously, exterior and interior finishing, including window grills, window frames, doors, toilet fittings, veranda grills, main gate, collapsible gate are also being carried out. The experts are ensuring that the installations meet the required standards for quality, functionality, safety, and energy efficiency. Few works are still pending as on 31st March 2023.

8. Painting: The inside and outside painting are pending and scheduled to be carried out and completed by July/August 2023.

Current Status:

As of 31st March 2023, the construction of the school building is progressing well. The foundation and superstructure work are totally completed, though plumbing, electrical, exterior & interior finishing installations and inside – outside painting are still underway. The project team has been proactive in completing the same on schedule.

Next Steps:

1. Completion of Roof Work: Once the superstructure work is finished, the roofing work will be initiated to provide protection from weather conditions.

2. Interior and Exterior Finishing: Following the roof installation, the focus will shift to interior and exterior finishing, including flooring, painting, and landscaping.



VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsss7012@gmail.com • Web : www.vsss.org
Fb : www.facebook.com/vsssindia • Blog : vsssindia.blogspot.in

3. Handover and Inauguration: After the final touches, the completed school building will be handed over to the educational authorities for further operational preparations. An official inauguration ceremony will be organized to mark the successful completion of the project.

Following are the details as of 31st march 2023:



Date of Commencement of the project: 15th Jan 2022 (FY 21-22)

Estimated date of completion of the project: 20th Aug 2023 (FY 23- 24)

Estimated date of Inauguration: 27th Aug 2023

Estimated total Cost of the project: Approximately 65 Lakh to 70 lakh

Sharing some photographs of the various phases of the construction:

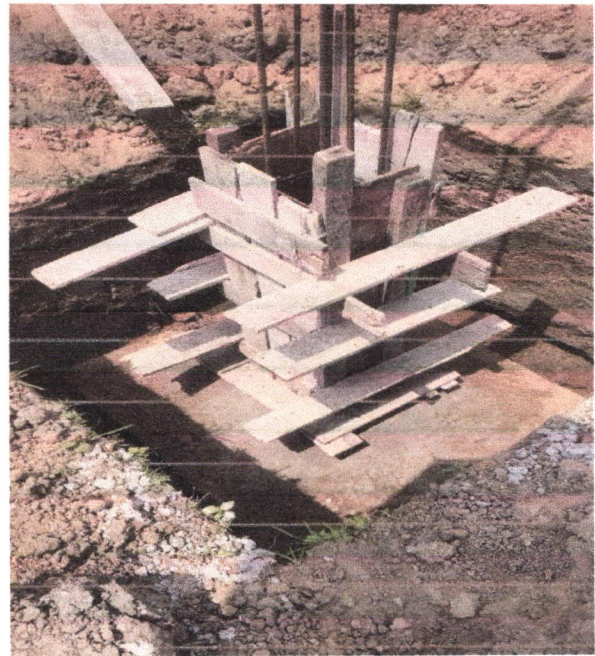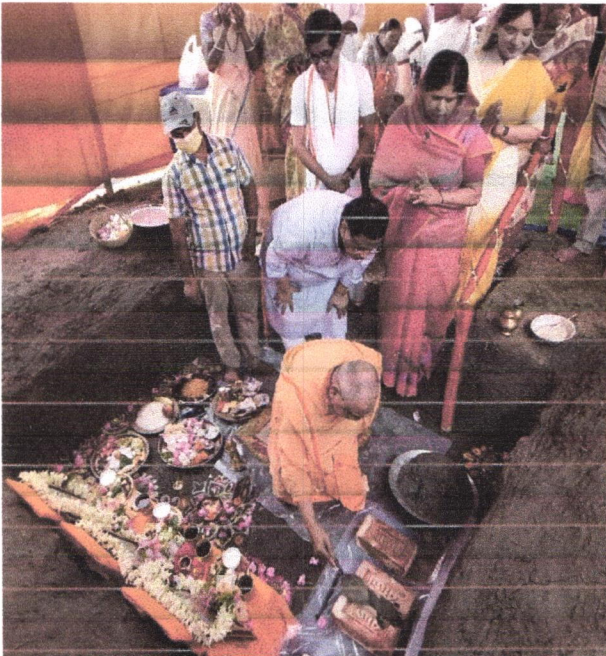



VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsst7012@gmail.com • Web : www.vsss.org
Fb : www.facebook.com/vsssindia • Blog : vsssindia.blogspot.in






VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vs557012@gmail.com • Web : www.v555.org
Fb : www.facebook.com/v555india • Blog : v555india.blogspot.in

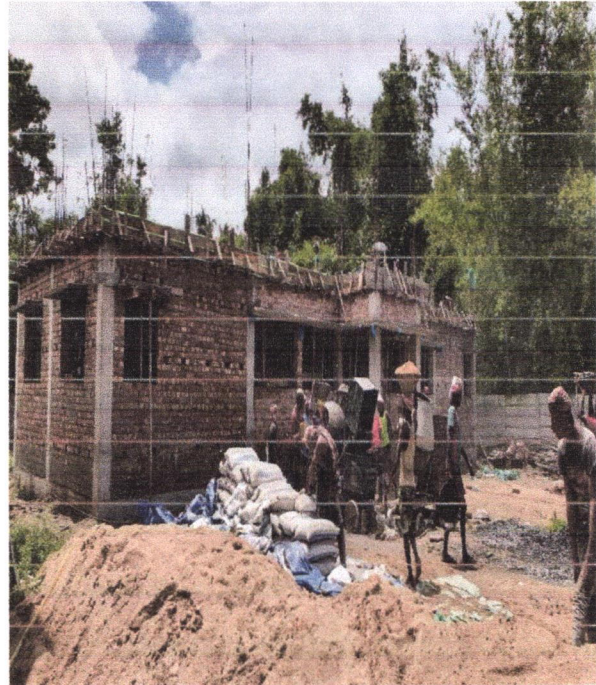




VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsst7012@gmail.com • Web : www.vsss.org
Fb : www.facebook.com/vsssindia • Blog : vsssindia.blogspot.in

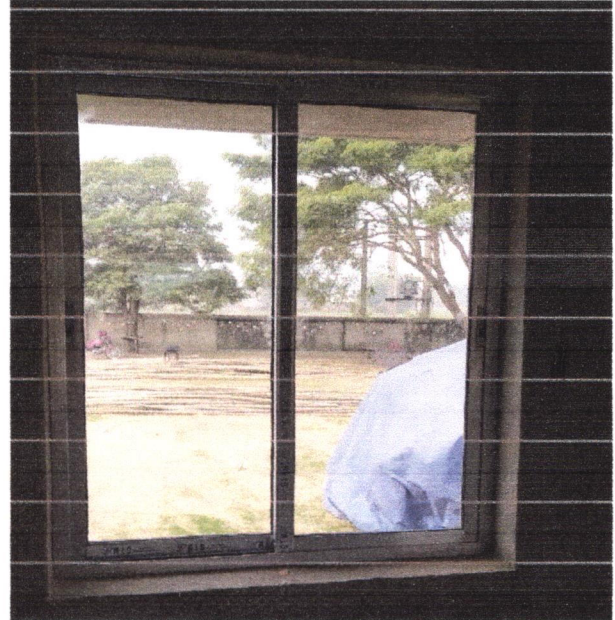

This above photo is showing the Current Construction stage as of 31st March 2023



VIVEKANANDA SWASTHYA SEVA SANGHA

(A Registered voluntary organisation for rural health care)

Regd. Office :
RC-20/11, Raghunathpur,
Kolkata-700 059

Working Centre :
CJ-142, Salt Lake, Sector-II
Kolkata-700 091, ☎ : (033) 4008 0771

Regn.no. SO048815 of 1985-1986, Email : vsss7012@gmail.com ● Web : www.vsss.org
Fb : www.facebook.com/vsssindia ● Blog : vsssindia.blogspot.in

Conclusion:

The construction of the school building, funded by Corporate Social Responsibility (CSR) fund of Udyogi Foundation Trust, 294, B.B Ganguly Street, 2nd Floor, Kolkata, has made significant progress within the specified timeline. The project team, along with the contractors and experts, aims to maintain the same level of dedication and commitment to ensure the timely completion of the construction. The initiative exemplifies the corporate and trust's commitment to social development through education.

Warm Regards,

Dr Gour Gopal Das
Chief Functionary
Vivekananda Swasthya Seva Sangha

